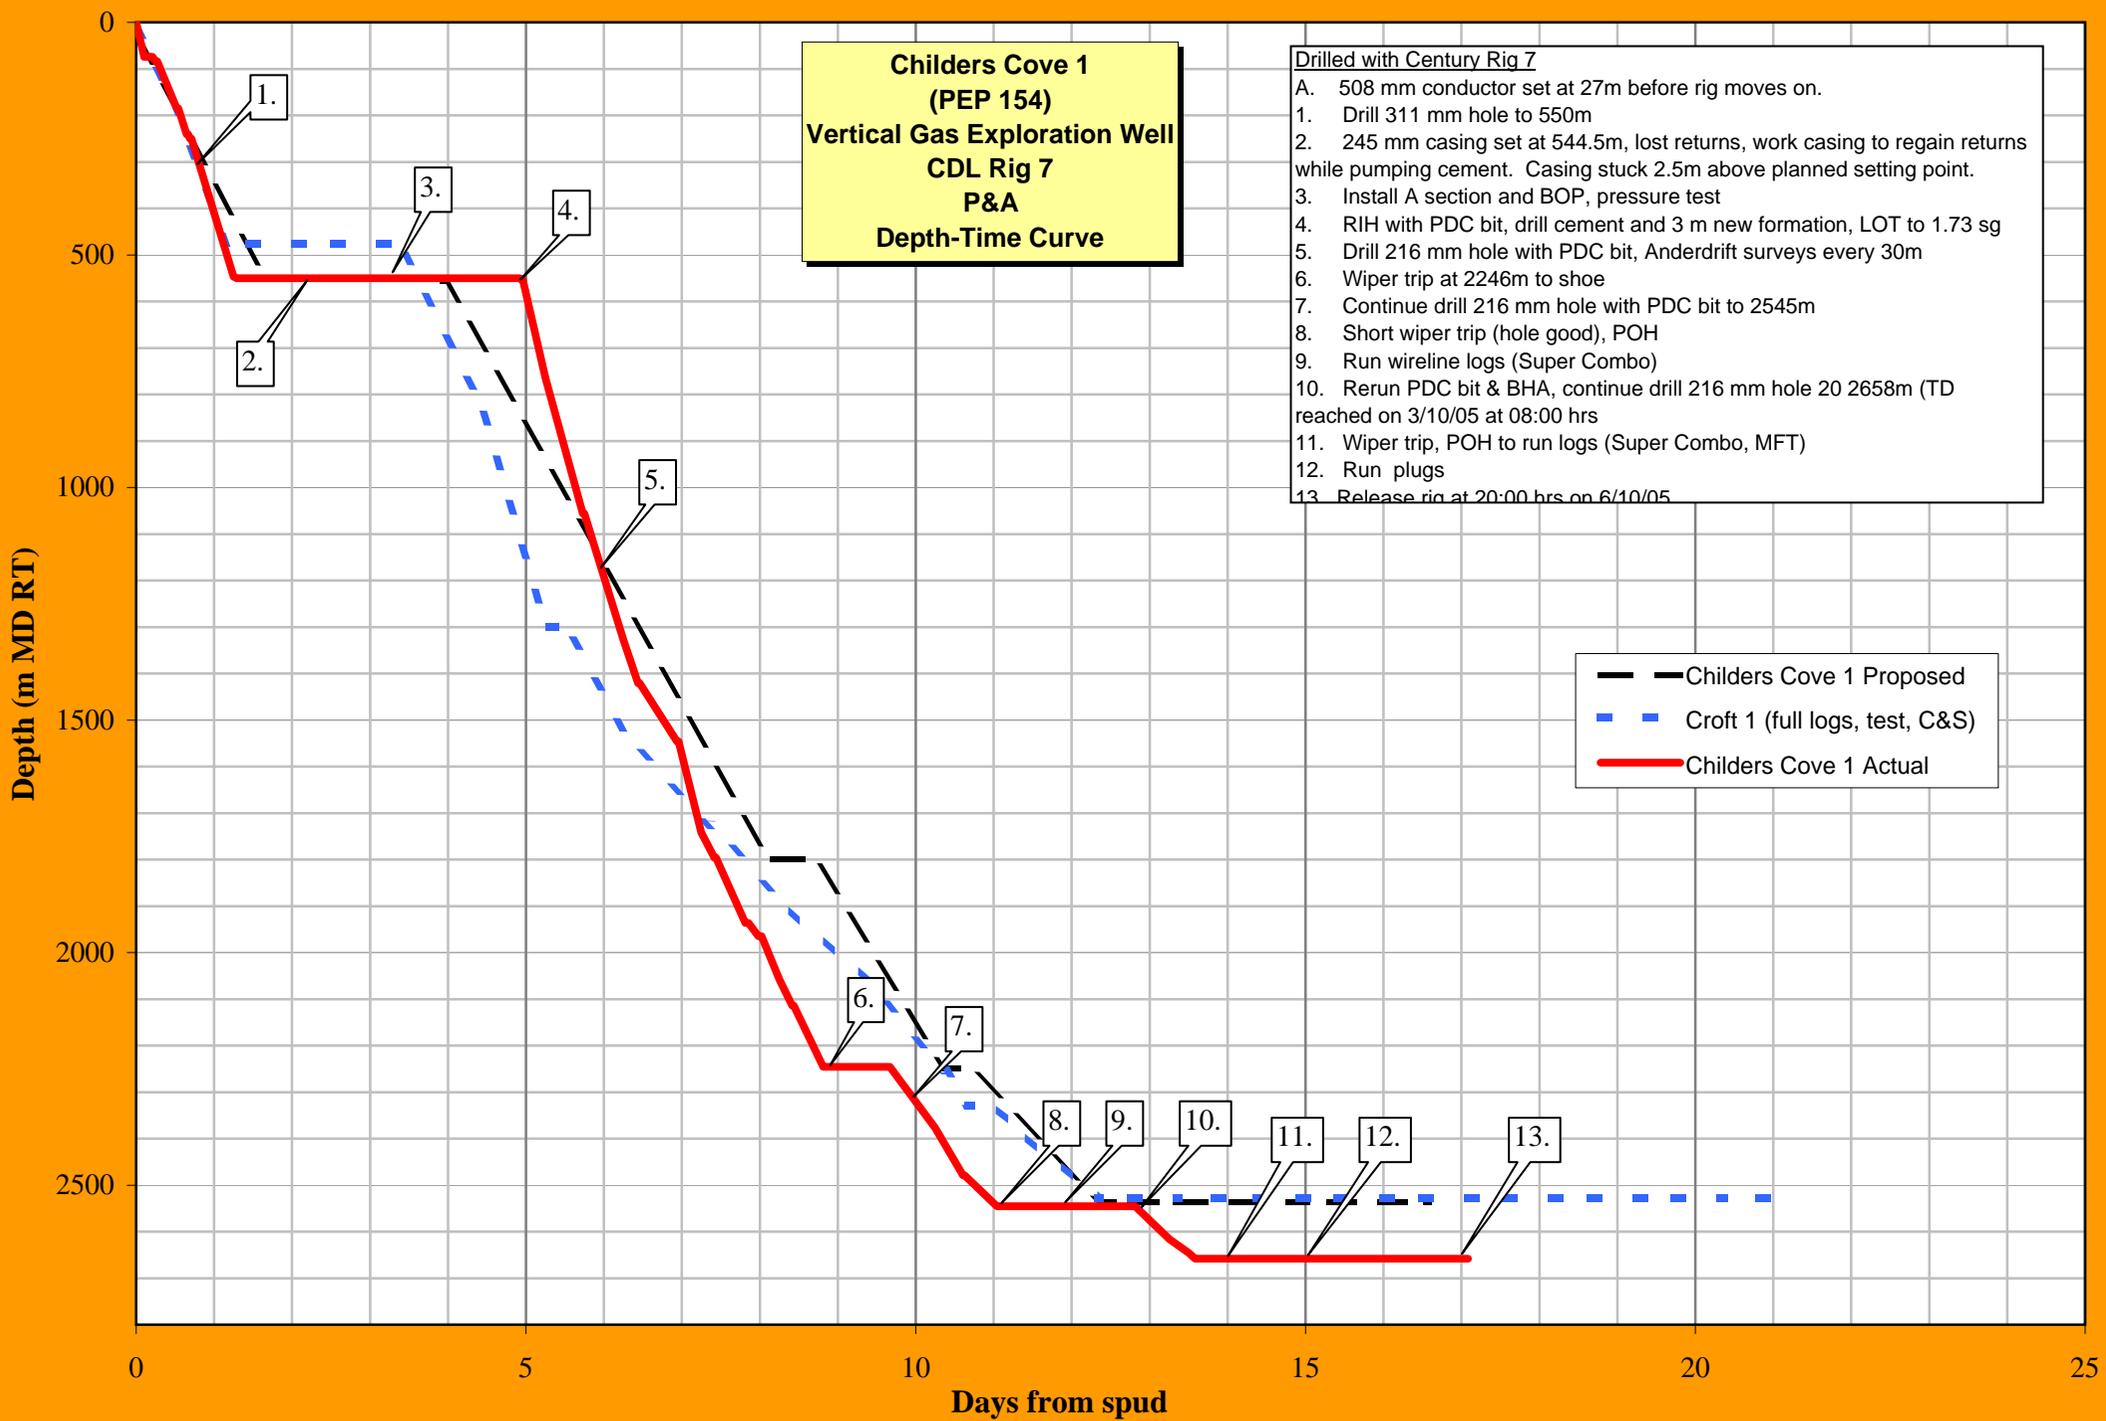


**Childers Cove 1  
(PEP 154)  
Vertical Gas Exploration Well  
CDL Rig 7  
P&A  
Depth-Time Curve**

- Drilled with Century Rig 7
- A. 508 mm conductor set at 27m before rig moves on.
  - 1. Drill 311 mm hole to 550m
  - 2. 245 mm casing set at 544.5m, lost returns, work casing to regain returns while pumping cement. Casing stuck 2.5m above planned setting point.
  - 3. Install A section and BOP, pressure test
  - 4. RIH with PDC bit, drill cement and 3 m new formation, LOT to 1.73 sg
  - 5. Drill 216 mm hole with PDC bit, Anderdrift surveys every 30m
  - 6. Wiper trip at 2246m to shoe
  - 7. Continue drill 216 mm hole with PDC bit to 2545m
  - 8. Short wiper trip (hole good), POH
  - 9. Run wireline logs (Super Combo)
  - 10. Rerun PDC bit & BHA, continue drill 216 mm hole 20 2658m (TD reached on 3/10/05 at 08:00 hrs
  - 11. Wiper trip, POH to run logs (Super Combo, MFT)
  - 12. Run plugs
  - 13. Release rig at 20:00 hrs on 6/10/05



**FIGURE 4**
