


Henry-2/2DW1ST1 Time versus Depth Curve

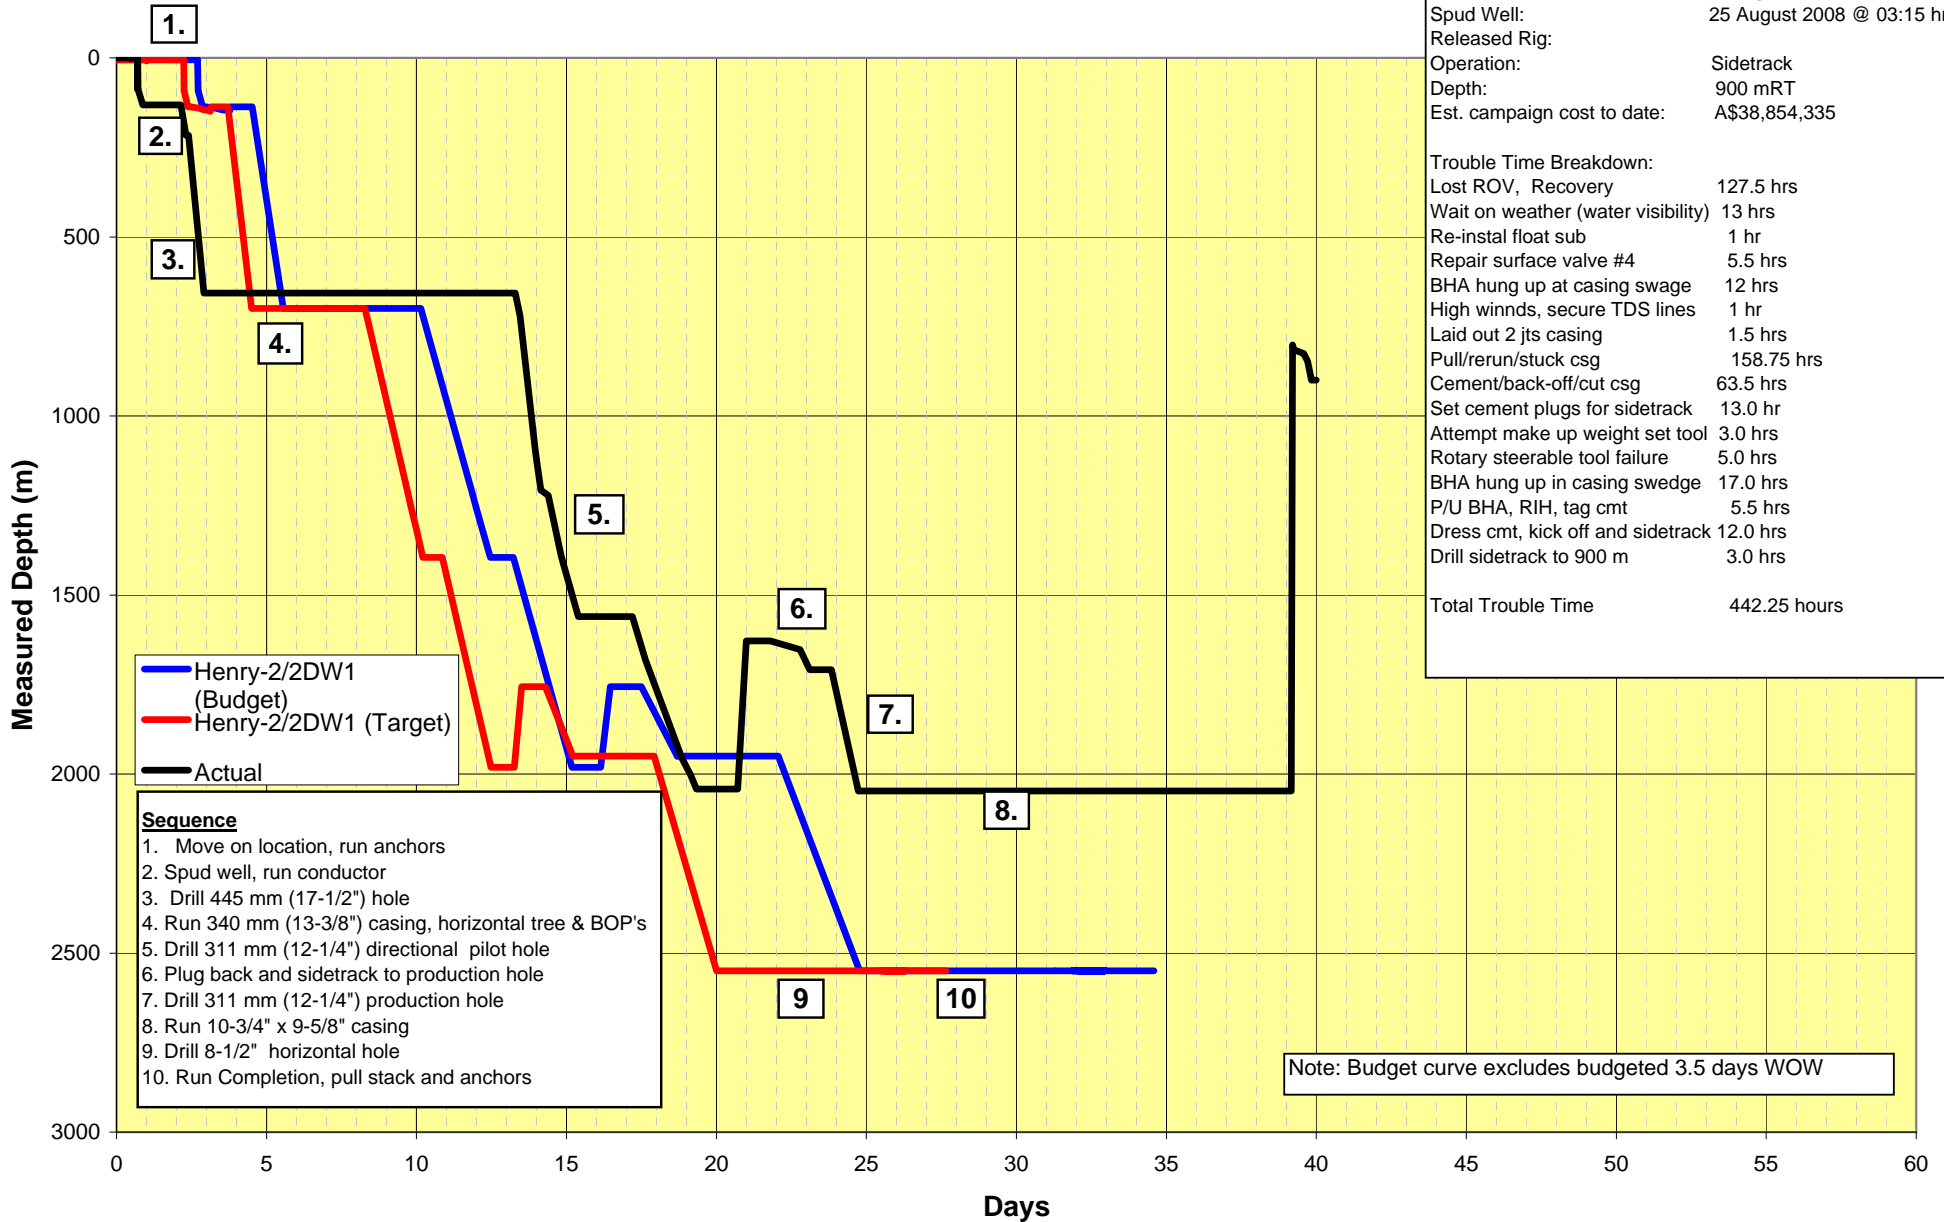

Henry-2/2DW1ST1 Friday 3rd October @ 0600hrs	
Commenced Well:	24 August 2008 @ 12:30 hrs
Spud Well:	25 August 2008 @ 03:15 hrs
Released Rig:	
Operation:	Sidetrack
Depth:	900 mRT
Est. campaign cost to date:	A\$38,854,335
Trouble Time Breakdown:	
Lost ROV, Recovery	127.5 hrs
Wait on weather (water visibility)	13 hrs
Re-install float sub	1 hr
Repair surface valve #4	5.5 hrs
BHA hung up at casing swage	12 hrs
High winnds, secure TDS lines	1 hr
Laid out 2 jts casing	1.5 hrs
Pull/rerun/stuck csg	158.75 hrs
Cement/back-off/cut csg	63.5 hrs
Set cement plugs for sidetrack	13.0 hr
Attempt make up weight set tool	3.0 hrs
Rotary steerable tool failure	5.0 hrs
BHA hung up in casing swedge	17.0 hrs
P/U BHA, RIH, tag cmt	5.5 hrs
Dress cmt, kick off and sidetrack	12.0 hrs
Drill sidetrack to 900 m	3.0 hrs
Total Trouble Time	442.25 hours
