GALLOWAY 1
TIME v DEPTH CURVE

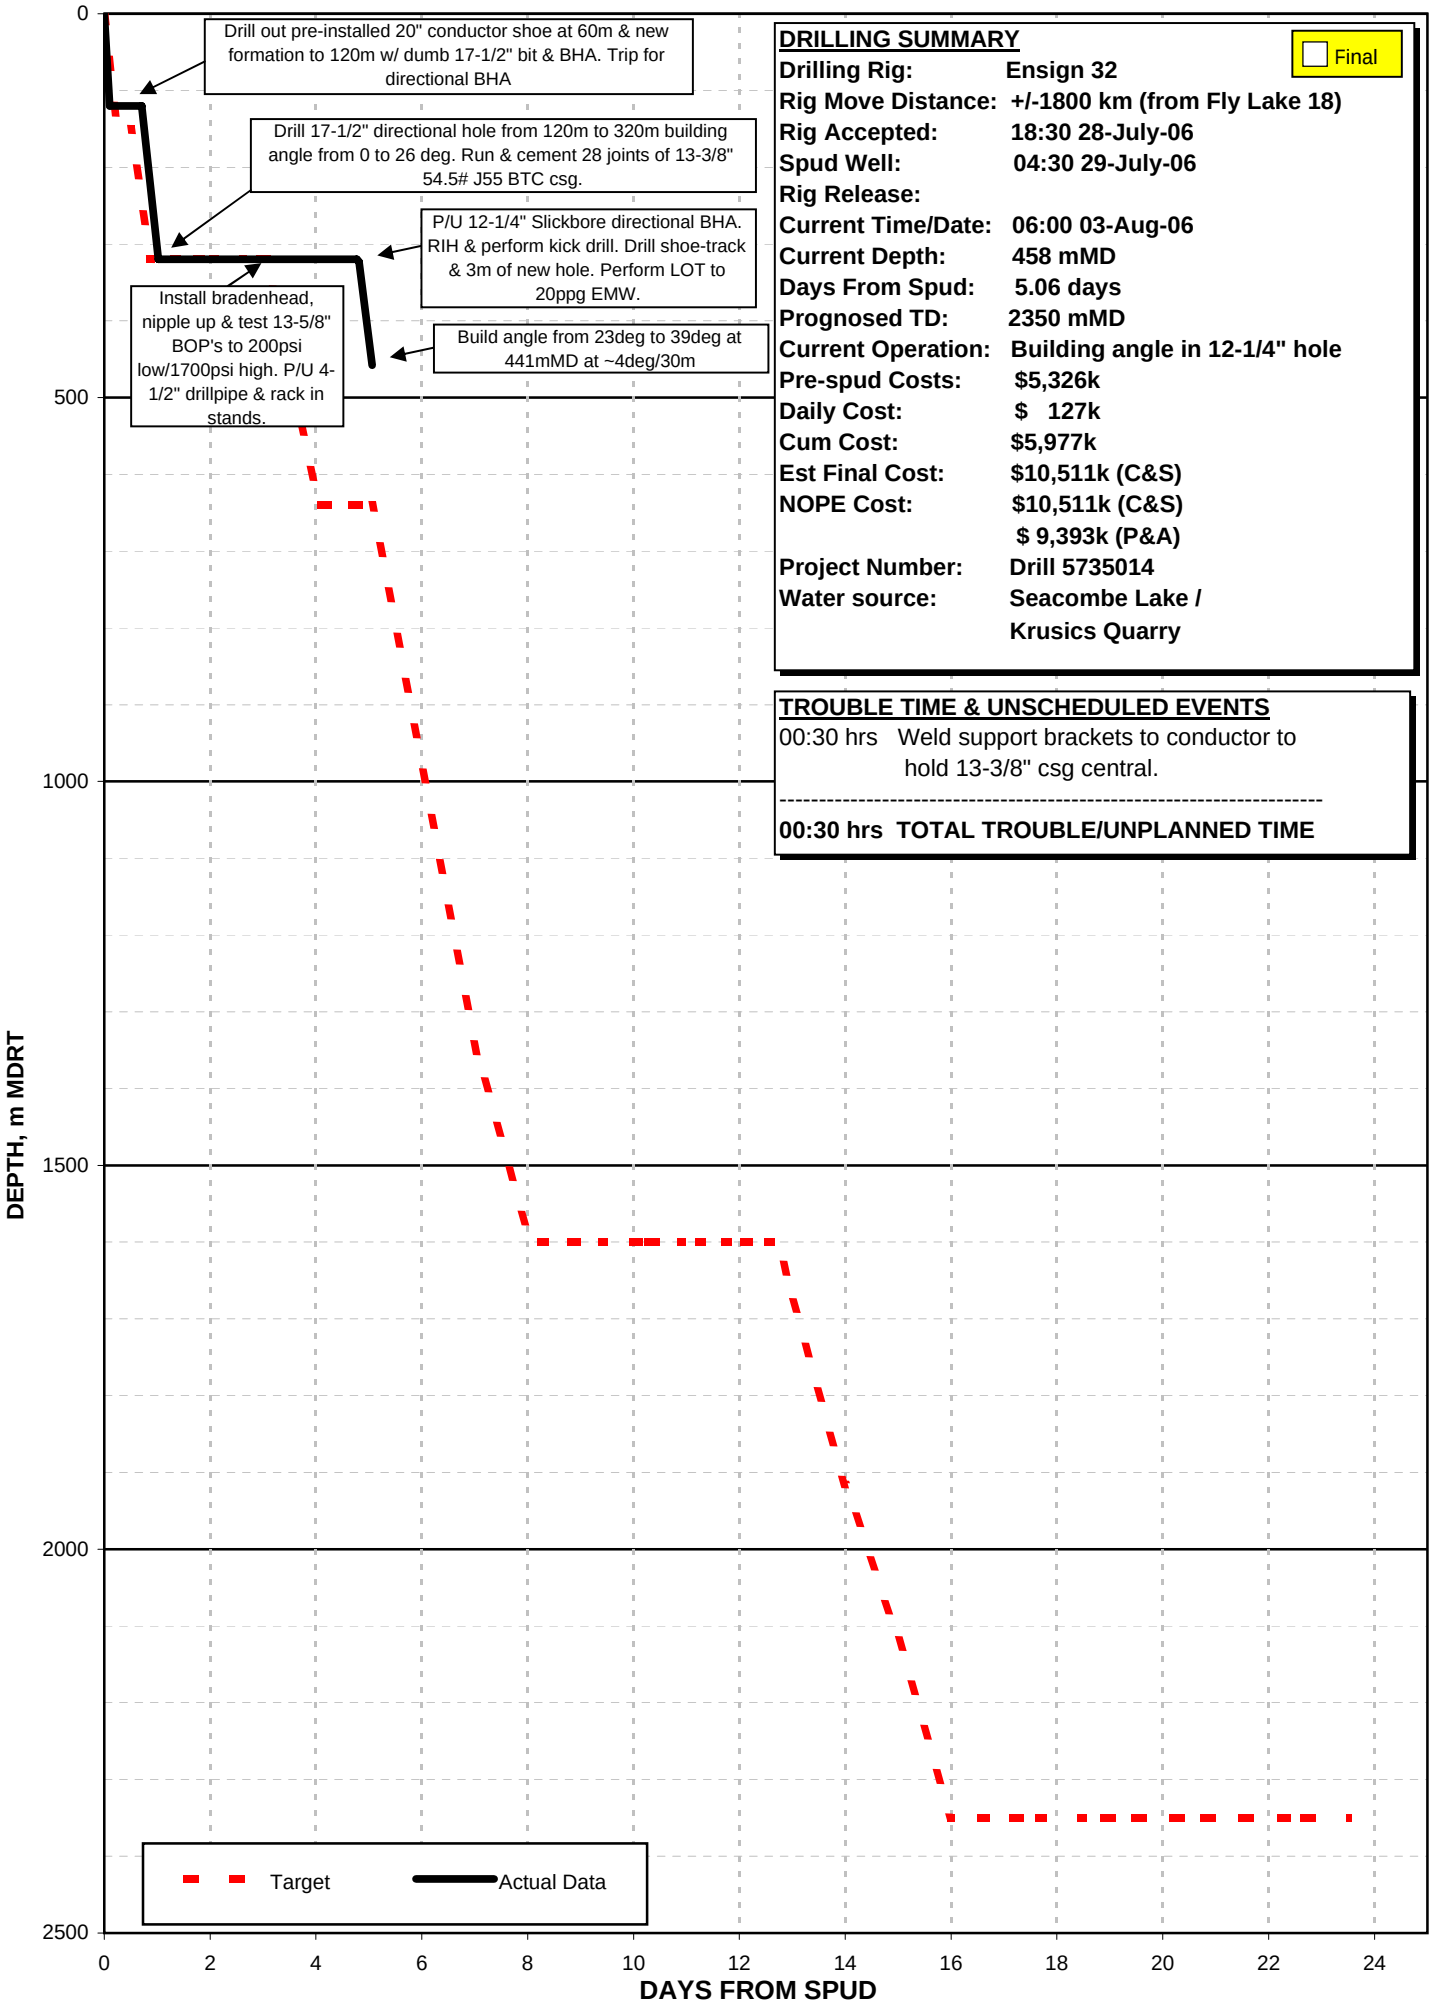

DRILLING SUMMARY

☐ Final

Drilling Rig:	Ensign 32
Rig Move Distance:	+/-1800 km (from Fly Lake 18)
Rig Accepted:	18:30 28-July-06
Spud Well:	04:30 29-July-06
Rig Release:	
Current Time/Date:	06:00 03-Aug-06
Current Depth:	458 mMD
Days From Spud:	5.06 days
Prognosed TD:	2350 mMD
Current Operation:	Building angle in 12-1/4" hole
Pre-spud Costs:	$5,326k
Daily Cost:	$ 127k
Cum Cost:	$5,977k
Est Final Cost:	$10,511k (C&S)
NOPE Cost:	$10,511k (C&S)
	$ 9,393k (P&A)
Project Number:	Drill 5735014
Water source:	Seacombe Lake / Krusics Quarry

TROUBLE TIME & UNSCHEDULED EVENTS

00:30 hrs Weld support brackets to conductor to hold 13-3/8" csg central.

00:30 hrs TOTAL TROUBLE/UNPLANNED TIME
