GALLOWAY 1
TIME v DEPTH CURVE

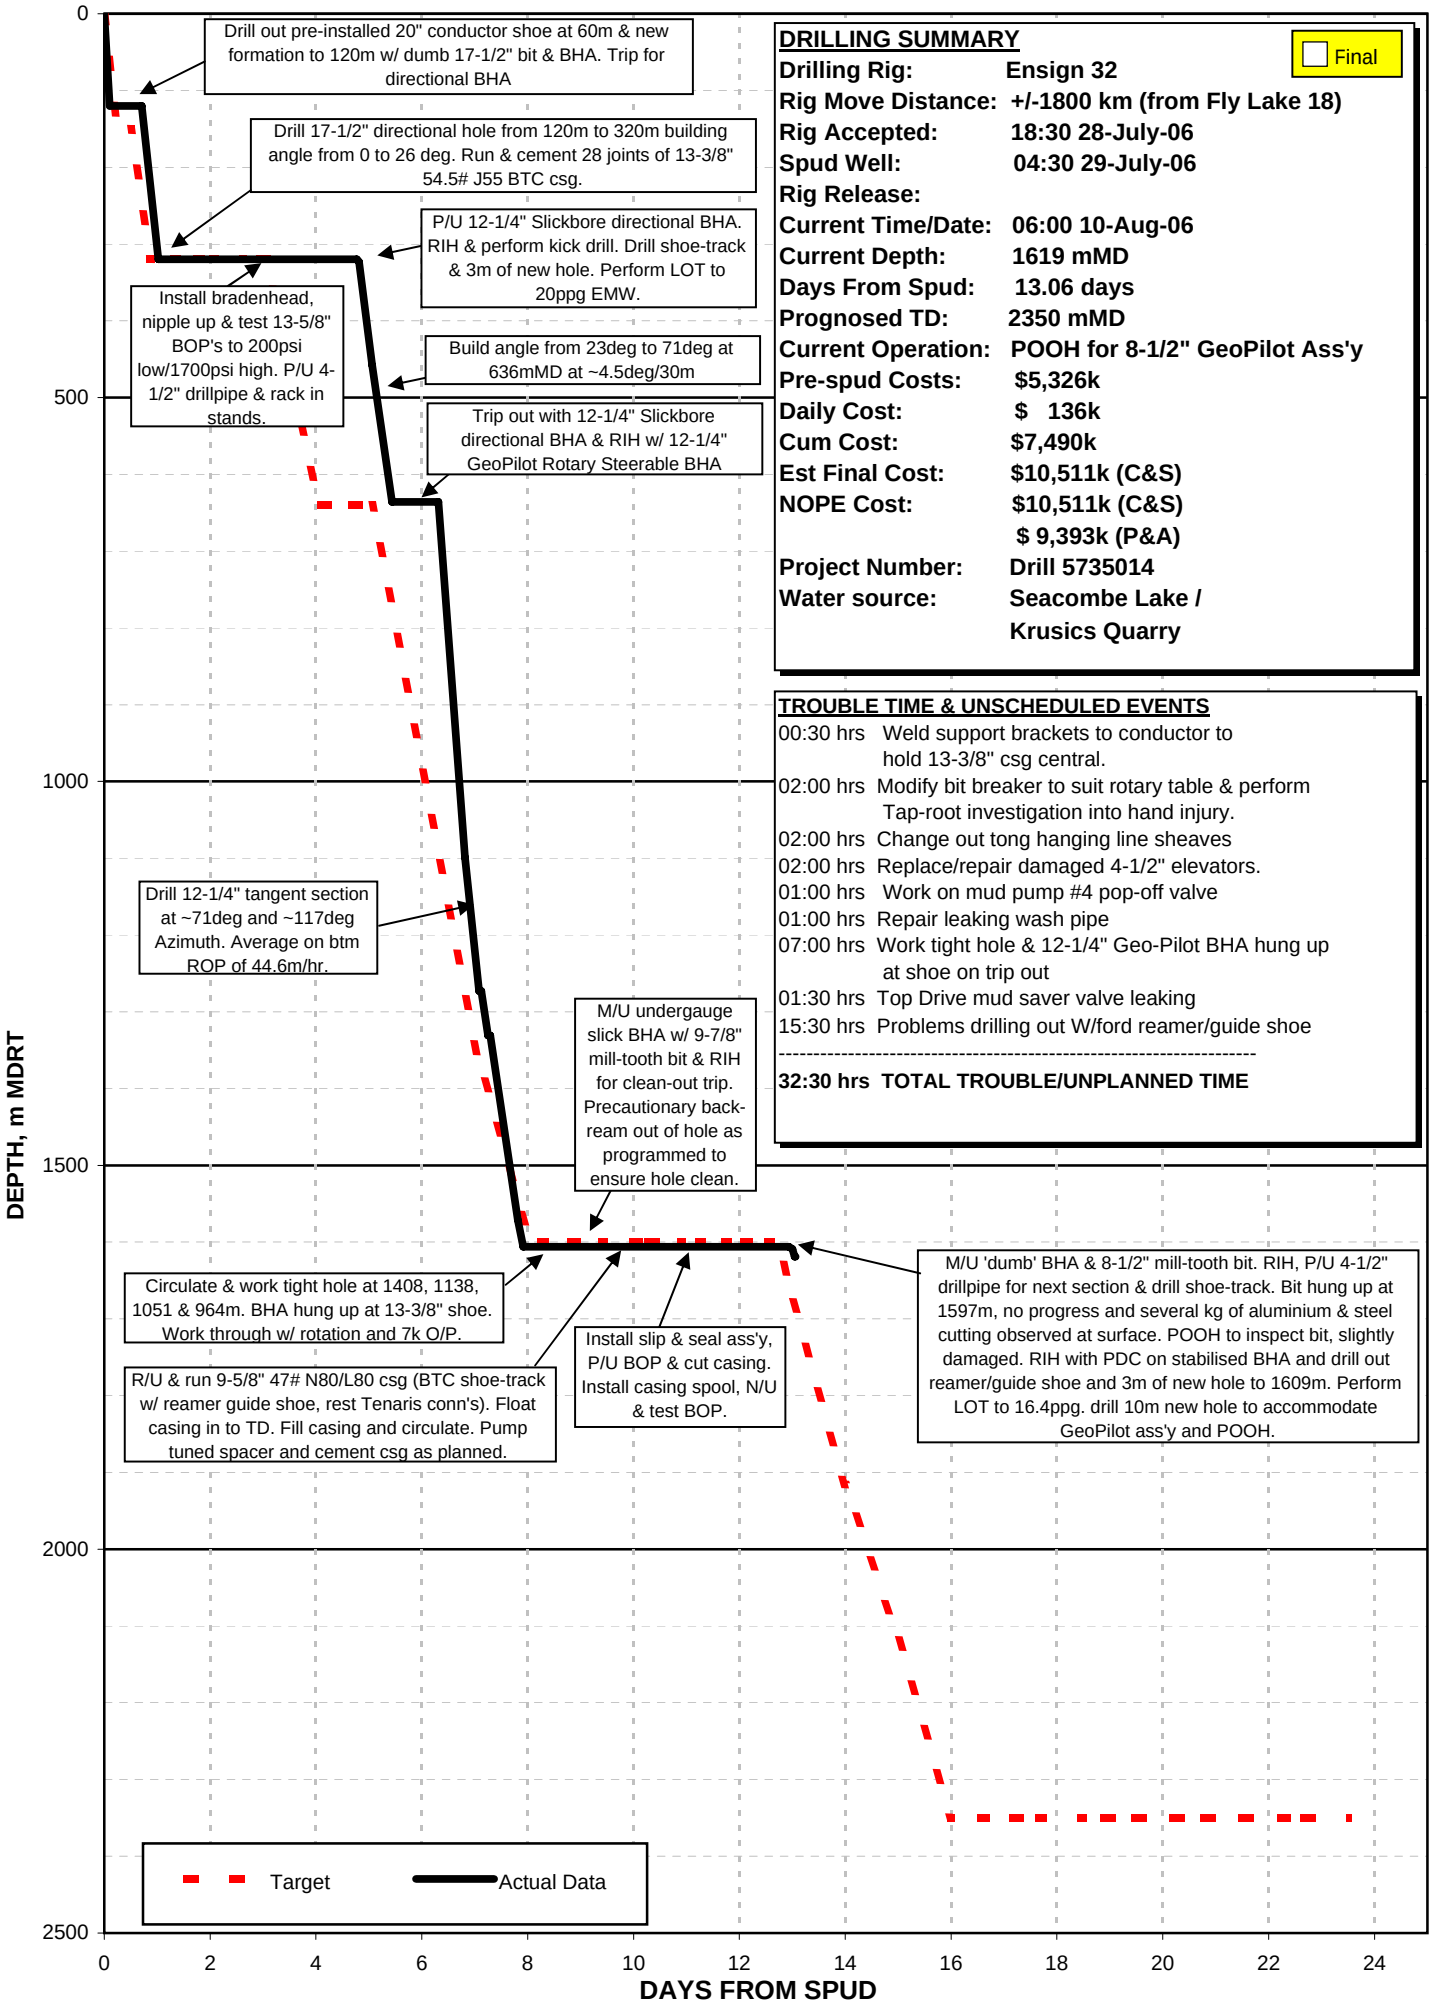

DRILLING SUMMARY

☐ Final

Drilling Rig:	**Ensign 32**
Rig Move Distance:	**+/-1800 km (from Fly Lake 18)**
Rig Accepted:	**18:30 28-July-06**
Spud Well:	**04:30 29-July-06**
Rig Release:	
Current Time/Date:	**06:00 10-Aug-06**
Current Depth:	**1619 mMD**
Days From Spud:	**13.06 days**
Prognosed TD:	**2350 mMD**
Current Operation:	**POOH for 8-1/2" GeoPilot Ass'y**
Pre-spud Costs:	**$5,326k**
Daily Cost:	**$ 136k**
Cum Cost:	**$7,490k**
Est Final Cost:	**$10,511k (C&S)**
NOPE Cost:	**$10,511k (C&S)**
	$ 9,393k (P&A)
Project Number:	**Drill 5735014**
Water source:	**Seacombe Lake / Krusics Quarry**

TROUBLE TIME & UNSCHEDULED EVENTS

00:30 hrs	Weld support brackets to conductor to hold 13-3/8" csg central.
02:00 hrs	Modify bit breaker to suit rotary table & perform Tap-root investigation into hand injury.
02:00 hrs	Change out tong hanging line sheaves
02:00 hrs	Replace/repair damaged 4-1/2" elevators.
01:00 hrs	Work on mud pump #4 pop-off valve
01:00 hrs	Repair leaking wash pipe
07:00 hrs	Work tight hole & 12-1/4" Geo-Pilot BHA hung up at shoe on trip out
01:30 hrs	Top Drive mud saver valve leaking
15:30 hrs	Problems drilling out W/ford reamer/guide shoe
32:30 hrs	**TOTAL TROUBLE/UNPLANNED TIME**
