GALLOWAY 1
TIME v DEPTH CURVE

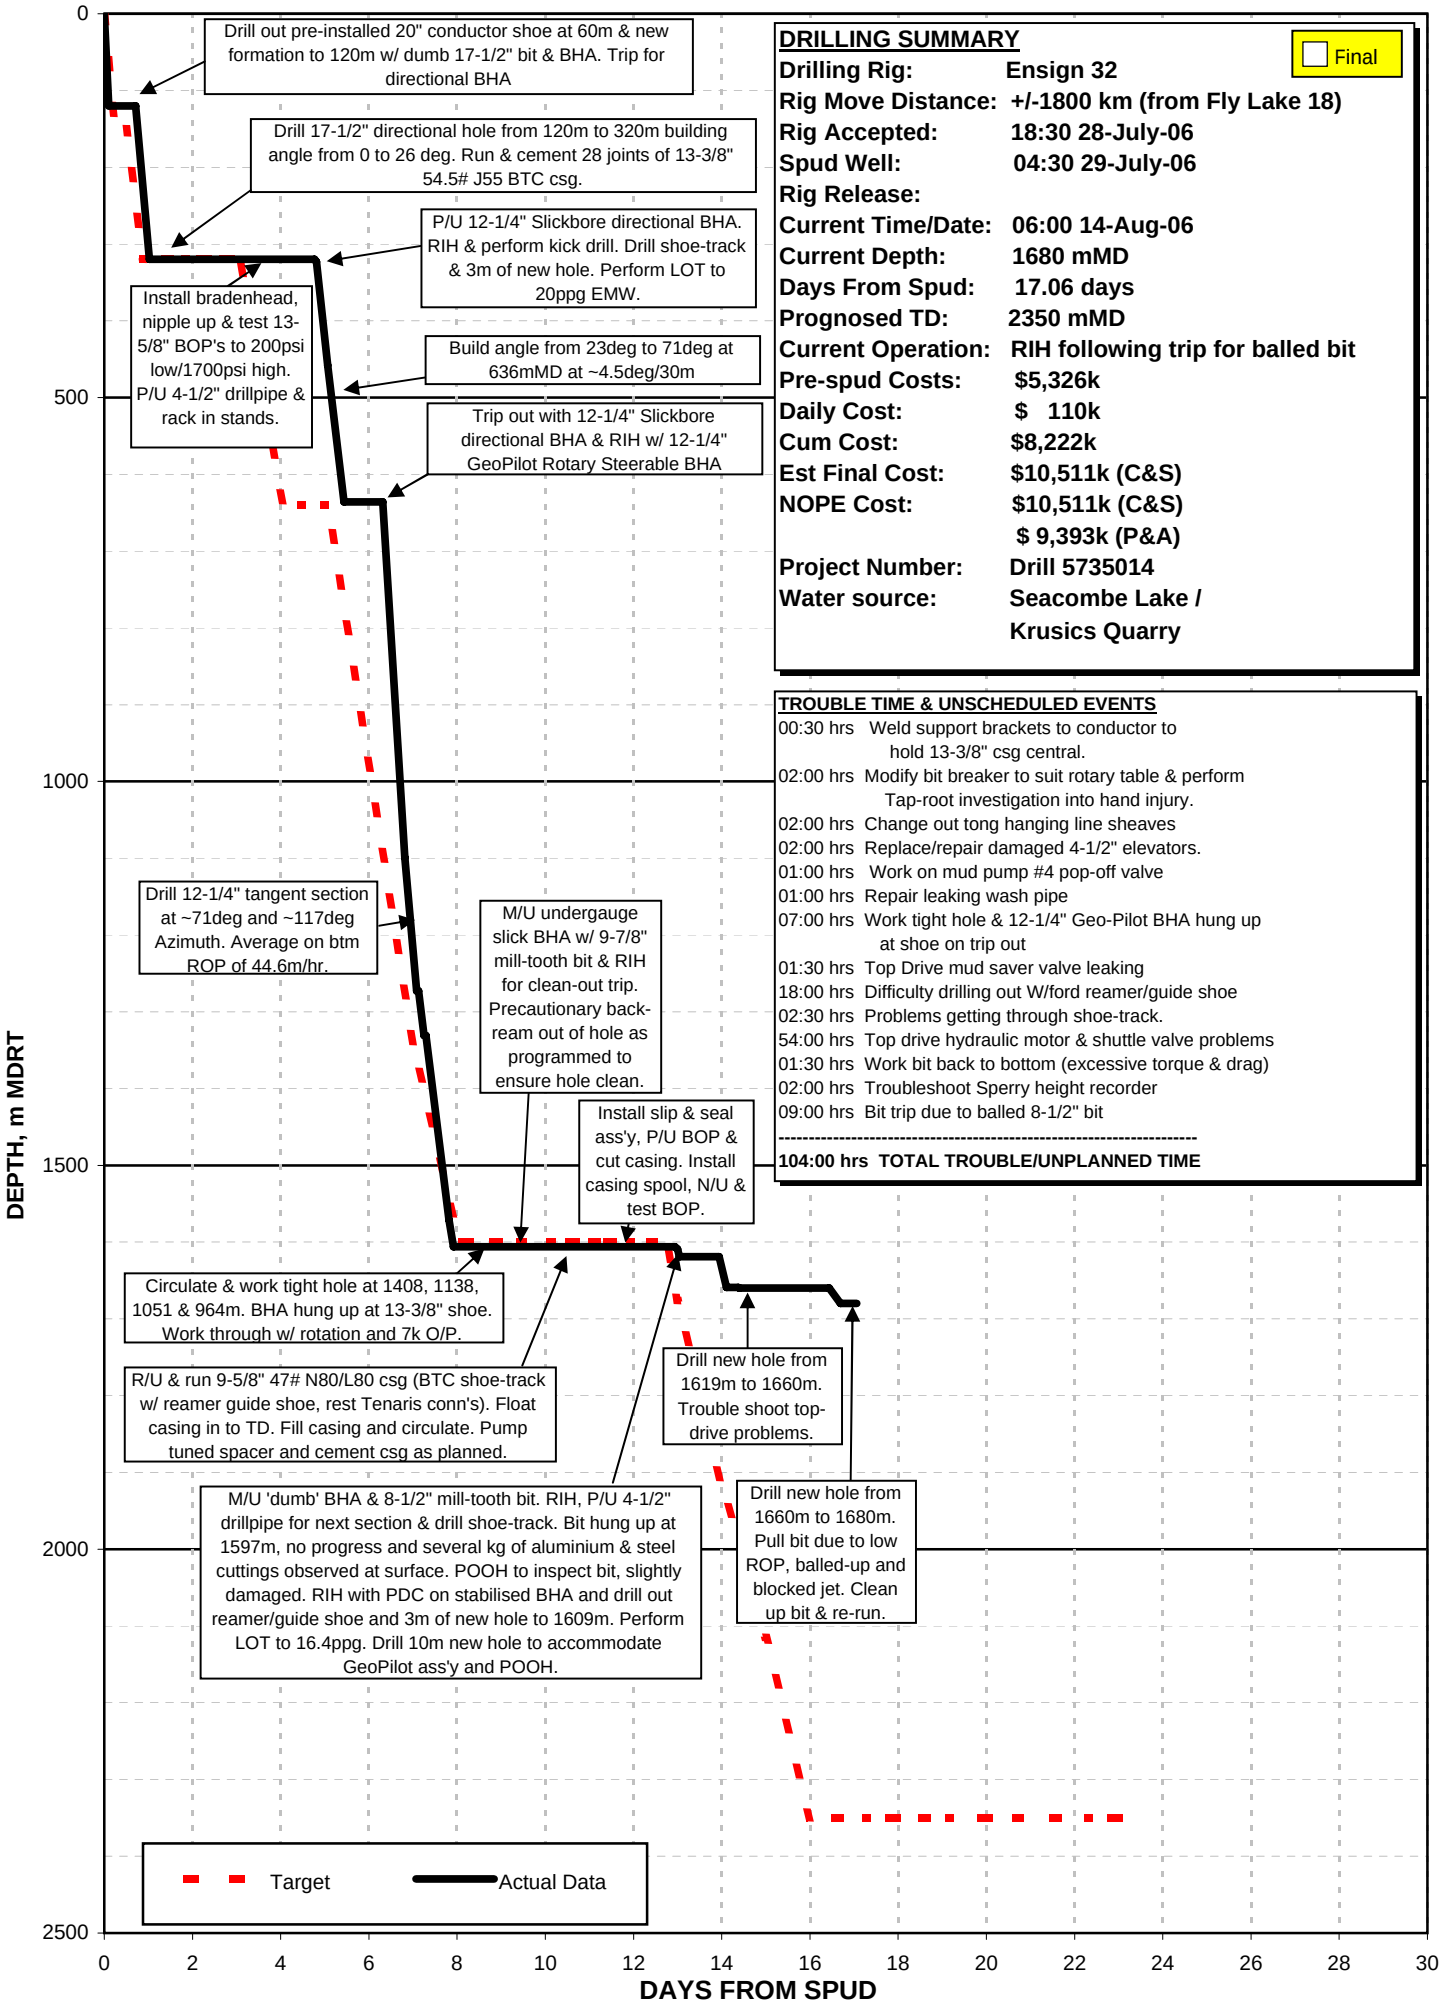

DRILLING SUMMARY

☐ Final

Drilling Rig:	Ensign 32
Rig Move Distance:	+/-1800 km (from Fly Lake 18)
Rig Accepted:	18:30 28-July-06
Spud Well:	04:30 29-July-06
Rig Release:	
Current Time/Date:	06:00 14-Aug-06
Current Depth:	1680 mMD
Days From Spud:	17.06 days
Prognosed TD:	2350 mMD
Current Operation:	RIH following trip for balled bit
Pre-spud Costs:	$5,326k
Daily Cost:	$ 110k
Cum Cost:	$8,222k
Est Final Cost:	$10,511k (C&S)
NOPE Cost:	$10,511k (C&S)
	$ 9,393k (P&A)
Project Number:	Drill 5735014
Water source:	Seacombe Lake / Krusics Quarry

TROUBLE TIME & UNSCHEDULED EVENTS

00:30 hrs Weld support brackets to conductor to hold 13-3/8" csg central.
02:00 hrs Modify bit breaker to suit rotary table & perform Tap-root investigation into hand injury.
02:00 hrs Change out tong hanging line sheaves
02:00 hrs Replace/repair damaged 4-1/2" elevators.
01:00 hrs Work on mud pump #4 pop-off valve
01:00 hrs Repair leaking wash pipe
07:00 hrs Work tight hole & 12-1/4" Geo-Pilot BHA hung up at shoe on trip out
01:30 hrs Top Drive mud saver valve leaking
18:00 hrs Difficulty drilling out W/ford reamer/guide shoe
02:30 hrs Problems getting through shoe-track.
54:00 hrs Top drive hydraulic motor & shuttle valve problems
01:30 hrs Work bit back to bottom (excessive torque & drag)
02:00 hrs Troubleshoot Sperry height recorder
09:00 hrs Bit trip due to balled 8-1/2" bit

104:00 hrs TOTAL TROUBLE/UNPLANNED TIME
