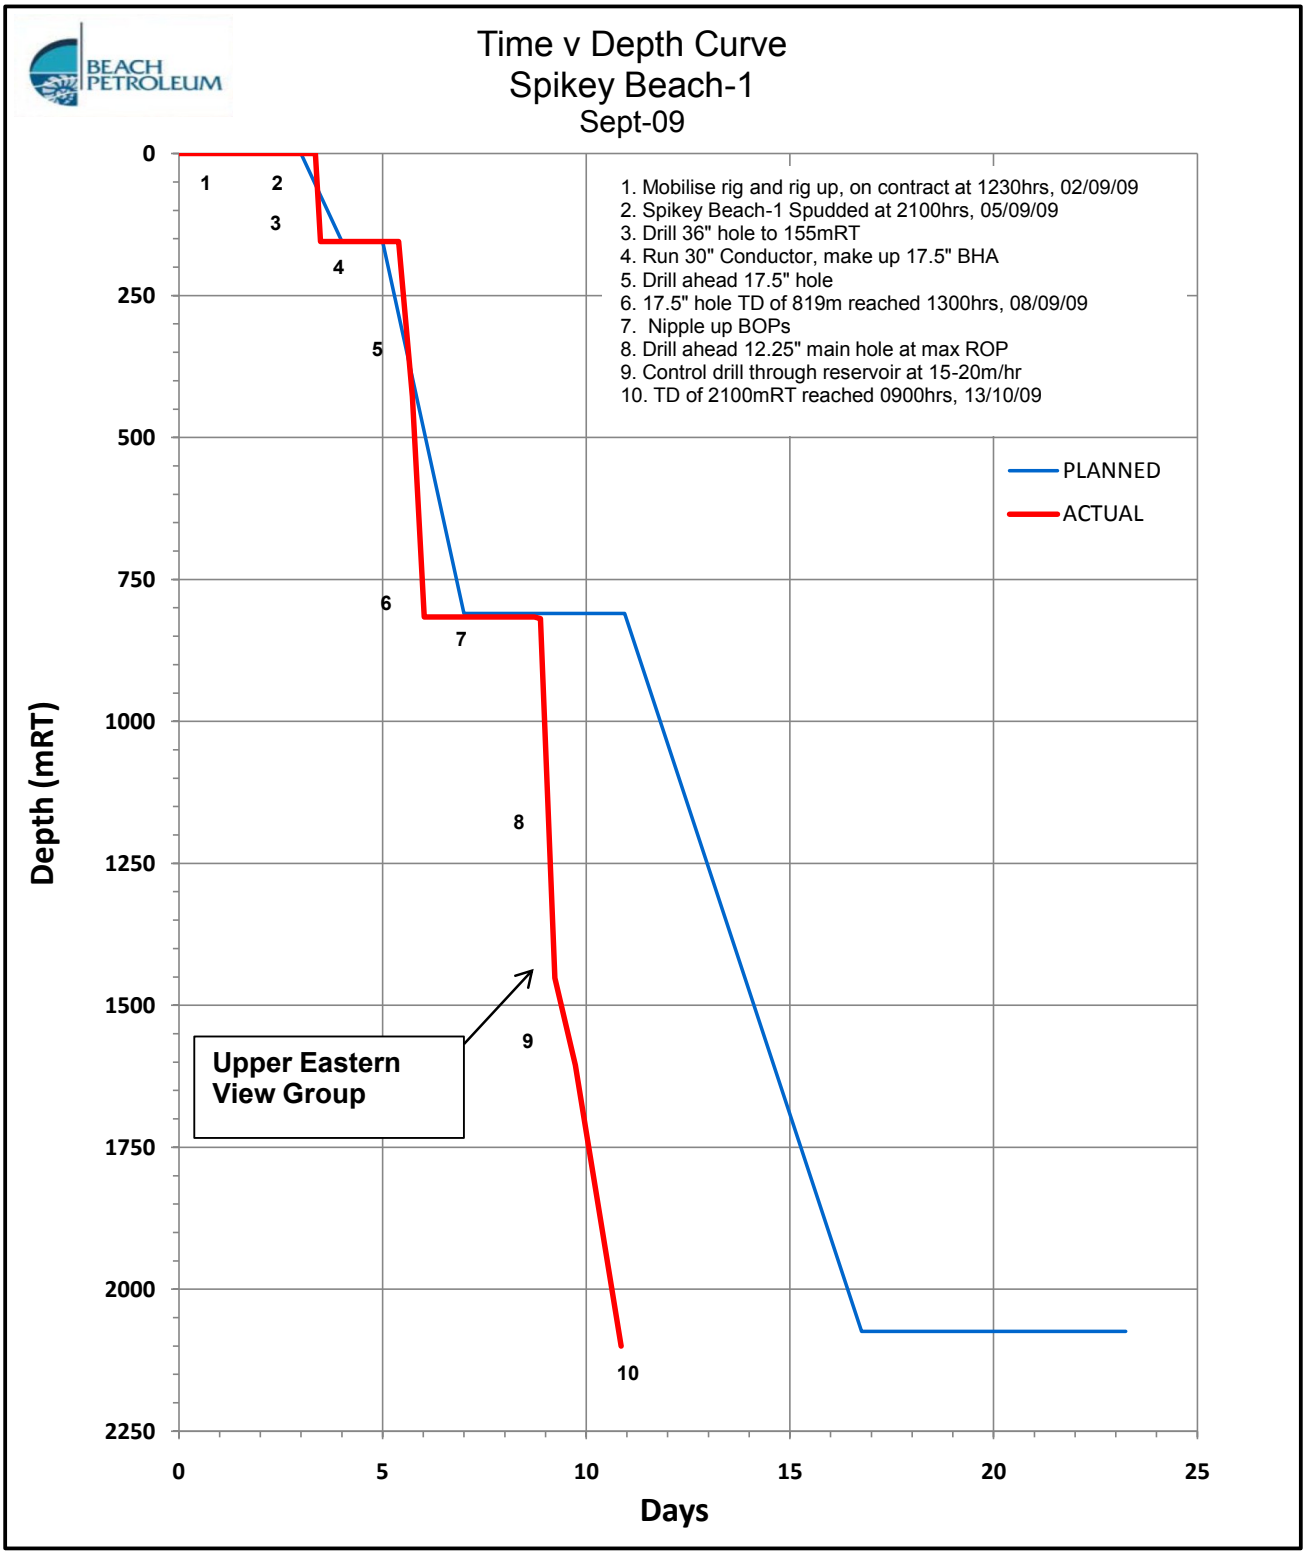
BEACH PETROLEUM
Time v Depth Curve
Spikey Beach-1
Sept-09
1. Mobilise rig and rig up, on contract at 1230hrs, 02/09/09
2. Spikey Beach-1 Spudded at 2100hrs, 05/09/09
3. Drill 36" hole to 155mRT
4. Run 30" Conductor, make up 17.5" BHA
5. Drill ahead 17.5" hole
6. 17.5" hole TD of 819m reached 1300hrs, 08/09/09
7. Nipple up BOPs
8. Drill ahead 12.25" main hole at max ROP
9. Control drill through reservoir at 15-20m/hr
10. TD of 2100mRT reached 0900hrs, 13/10/09
PLANNED
ACTUAL
Upper Eastern View Group
Depth (mRT)
Days
0
250
500
750
1000
1250
1500
1750
2000
2250
0
5
10
15
20
25
